Project plan: the Riverside Community Kitchen

Executive Summary and Authorisation

This plan authorises the Riverside Community Kitchen. Its objective: Open a community kitchen that serves 200 meals a week. The sponsor is Riverside Trust. The declared budget is USD 48,000.00. The critical path runs 40 periods, with 3 critical activities. The plan carries the charter, scope, work breakdown, schedule, cost, assignments and risks; a record that is missing is named rather than guessed.

Project Charter

The charter authorises the Riverside Community Kitchen under Riverside Trust. The project manager is Alex Rivera. The declared budget is USD 48,000.00. Work starts on 2026-01-05. It is due on 2026-06-30.

Field	Value
Title	the Riverside Community Kitchen
Objective	Open a community kitchen that serves 200 meals a week.
Sponsor	Riverside Trust
Project manager	Alex Rivera
Budget	USD 48,000.00
Start	2026-01-05
End	2026-06-30

Scope and Exclusions

The scope declares 2 included items, 1 exclusion and 2 deliverables. The WBS decomposes the deliverables; the exclusions bound the work the project will not do.

Direction	Item
In scope	Kitchen fit-out
In scope	Permit applications
Out of scope	Delivery service

Direction	Item
Deliverable	Kitchen open
Deliverable	Permit issued

Work Breakdown Structure

The WBS carries 4 nodes and 4 work packages. Each work package states an owner, a cost and the test that shows it is complete; the parent nodes carry the roll-up.


ID	Work package	Owner	Cost	Acceptance
A1	Design the kitchen	Architect	USD 6,000.00	Drawings signed
A2	Apply for the permit	Project manager	USD 2,000.00	Permit issued
A3	Fit out the kitchen	Builder	USD 30,000.00	Handover signed
A4	Install equipment	Supplier	USD 10,000.00	Equipment commissioned

Schedule

The schedule carries 4 activities. The critical path runs 40 periods and carries 3 critical activities. Early and late dates and float are the frozen method's own values; an activity with float is not on the critical path.


ID	Activity	Duration	ES	EF	LS	LF	Float	Critical
A1	Design	10.0	0	10.0	5.0	15.0	5.0	no
A2	Permit	15.0	0	15.0	0.0	15.0	0.0	yes
A3	Fit out	20.0	15.0	35.0	15.0	35.0	0.0	yes
A4	Install	5.0	35.0	40.0	35.0	40.0	0.0	yes

Schedule chart

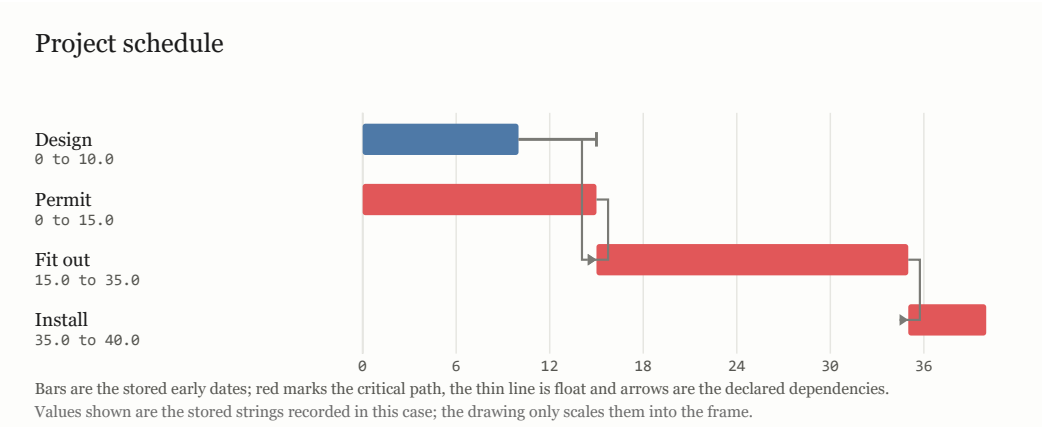


Project schedule

Activity network

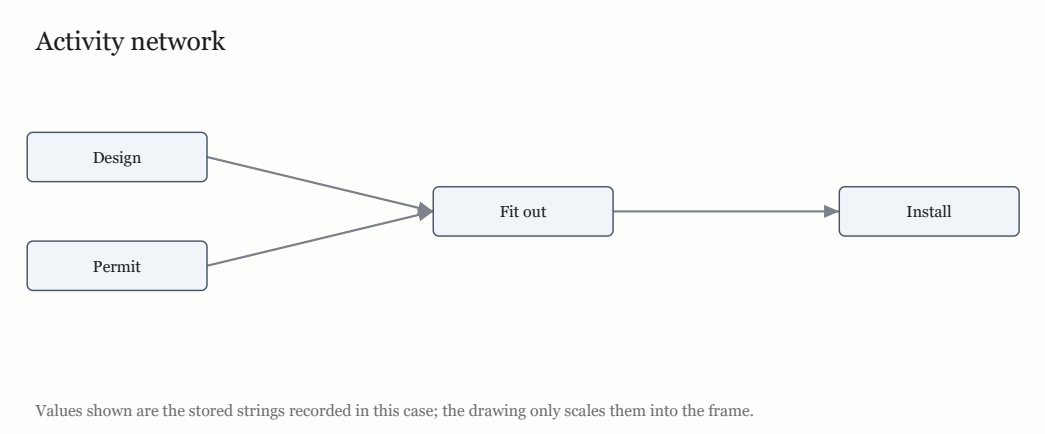

Activity network

Planned completion

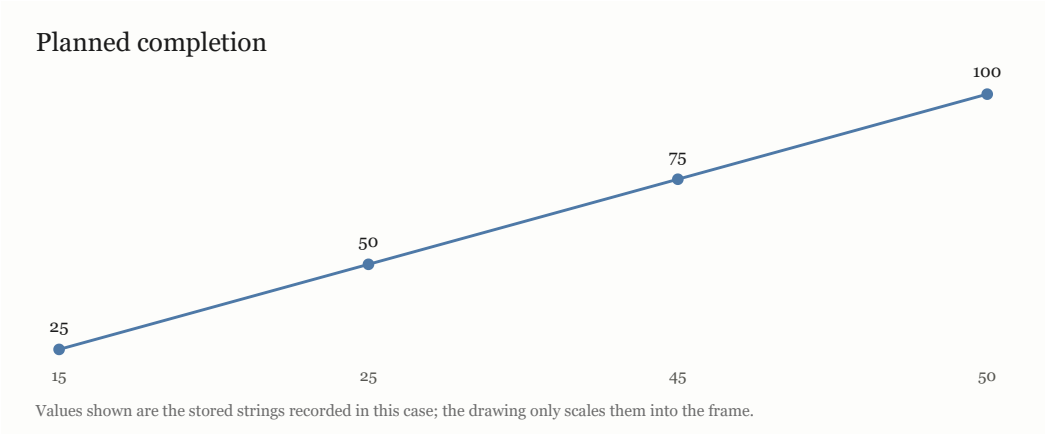

Planned completion curve

Dated Schedule

Dates count one declared period as one working day, Monday to Friday, from the declared start date of 2026-01-05. A finish is the last working day of the activity; weekends are a gap and no holiday is inferred.


ID	Activity	Start	Finish	Working days
A1	Design	2026-01-05	2026-01-16	12
A2	Permit	2026-01-05	2026-01-23	19
A3	Fit out	2026-01-26	2026-02-20	26
A4	Install	2026-02-23	2026-02-27	5

Resource-Levelled Schedule

The frozen resource-levelling method orders activities by early start, then longest duration, then id, and delays an activity until its declared resource has capacity. It adds 10 periods, so the plan finishes in 50 periods against 40 without resource limits. 10 periods were over capacity before levelling and 0 after; the peak demand was 2 before and 1 after.

ID	Activity	Levelled start	Levelled finish	Delay
A1	Design	15	25	15
A2	Permit	0	15	0
A3	Fit out	25	45	10
A4	Install	45	50	10

Resource load

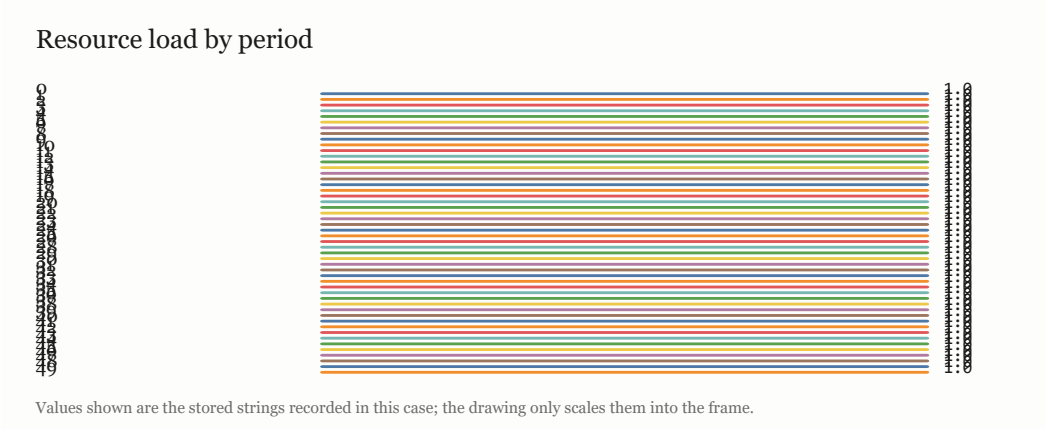

Resource load by period

Cost Plan

The WBS rolls 4 nodes up to a total of USD 48,000.00. The declared budget is USD 48,000.00; the variance is USD 0.00. Cost is carried by the work package, not by the activity; no estimate is added where the record declares none.

ID	Item	Cost
A1	Design the kitchen	USD 6,000.00
A2	Apply for the permit	USD 2,000.00
A3	Fit out the kitchen	USD 30,000.00
A4	Install equipment	USD 10,000.00
	Total	USD 48,000.00

Organisation and Assignments

The plan names 4 resources. Every activity carries exactly one accountable role and at least one responsible role in the RACI matrix; a blank cell or a missing role is a named gap, not an inferred assignment.

Name	Role	Capacity
Architect	Design	1.0
Project manager	Management	1.0
Builder	Build	1.0
Supplier	Equipment	1.0

RACI Matrix

The matrix names, for every activity, the roles the record declares as responsible and accountable, and the consulted or informed roles it states.

Activity	Name	Design	Management	Build	Equipment
A1	Design	R	A		
A2	Permit		A		
A3	Fit out		A	R	
A4	Install		A		R

Risk Register

The register carries 1 risk. Likelihood and impact are labels, not probabilities, and each risk states a response and an owner. No risk score or expected loss is computed.

ID	Risk	Likelihood	Impact	Response	Owner
R1	Permit delay	Medium	High	Apply early	Project manager

Governance and Change Control

The sponsor chairs a monthly review with the project manager Any scope change is approved in writing by the sponsor Decisions above the stated change threshold go to the sponsor; decisions below it stay with the project manager. The plan records the arrangement the student declared and adds no approval route of its own.

Monitoring and Success Measures

Progress is judged against 1 success measure, 1 assumption and 1 constraint. A success measure without a baseline is reported as stated, not converted into a target.

Item	Type
200 meals a week by month six	success measure
The lease is signed before work starts	assumption
The kitchen must open before June	constraint

Limitations

The plan is limited to the record the student supplied. The CPM uses the declared single-point durations; PERT was not run unless the record asks for it. Costs are work-package estimates, not commitments. The plan does not assess procurement, financing or benefits beyond the declared success measures, and it does not rank the risks. The schedule and cost are tied to the WBS as recorded, so a changed scope changes both and must follow the change-control route above. A reader should treat the named gaps as open questions, not as conditions already met.

Conclusion

The plan states what the project delivers, how it is broken down, what it costs, who does the work and what could go wrong. The WBS rolls up to USD 48,000.00 against a declared budget of USD 48,000.00. The critical path is 40 periods over 4 activities.

References

No sources were used.
