
Project plan: the Riverside Community Kitchen

Project plan

This plan authorises the Riverside Community Kitchen.

- The paper carries the charter, scope, work breakdown, schedule, cost, assignments and risks.

The critical path runs 50 periods over 4 activities.

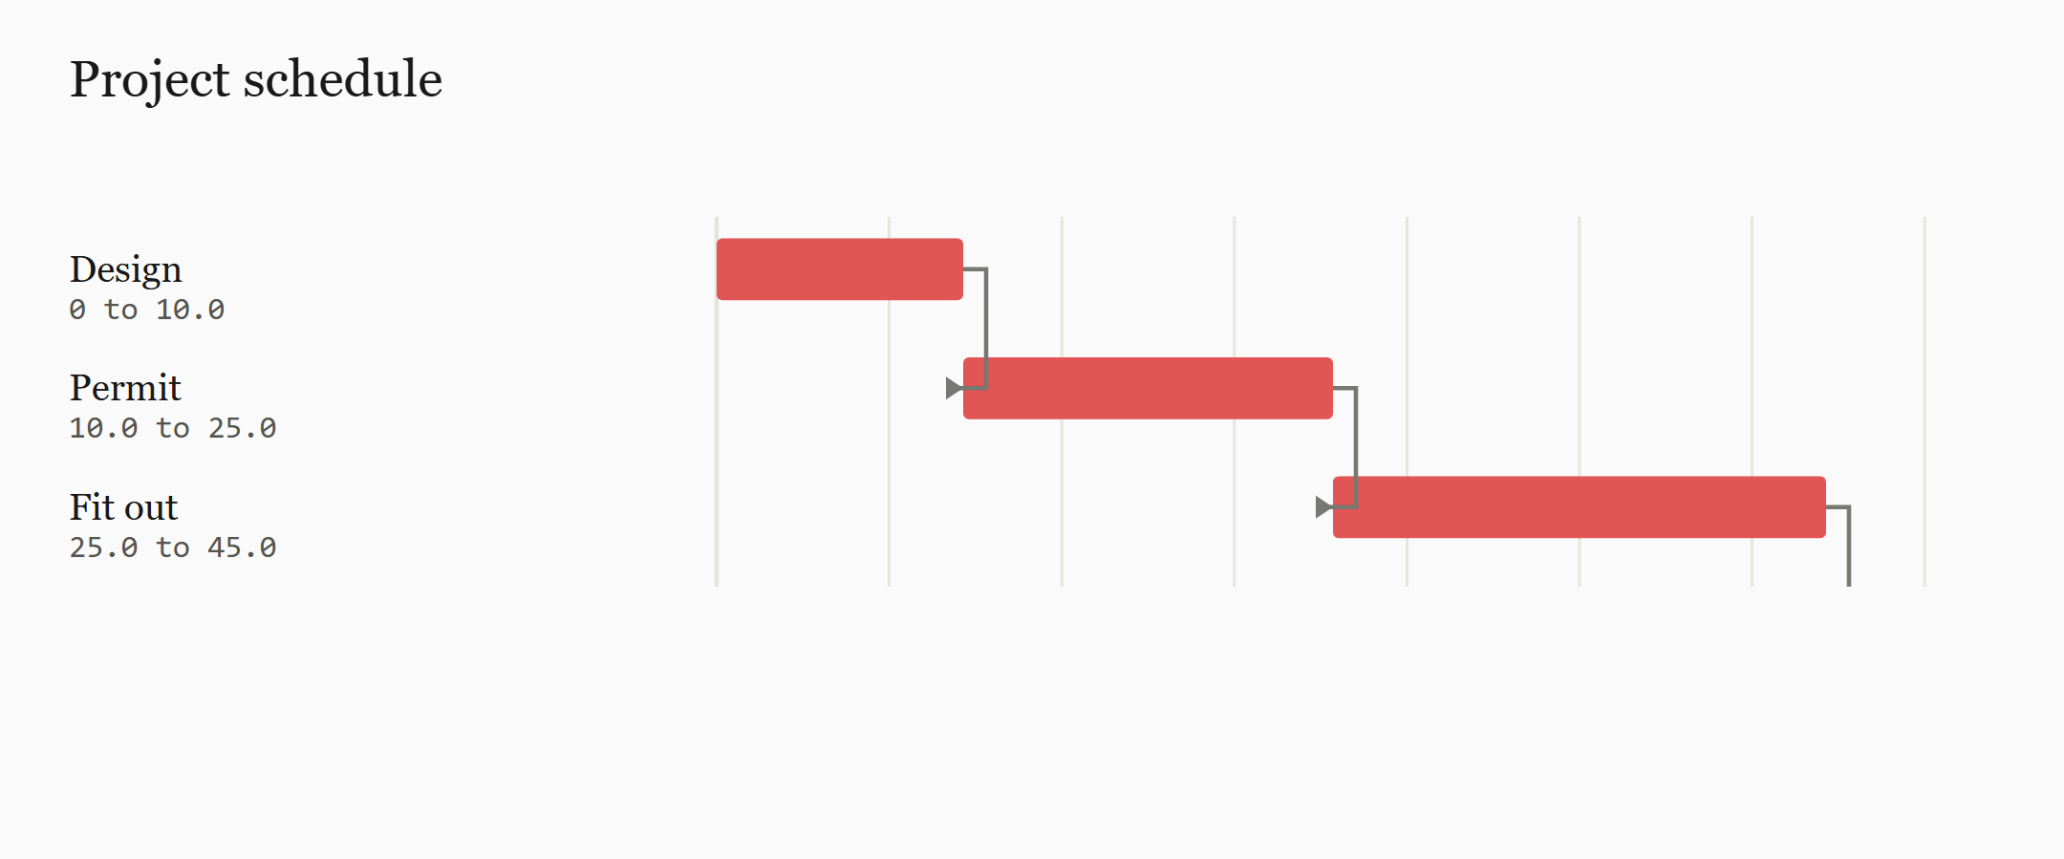

The WBS carries 4 nodes and 4 work packages.

ID	Work package	Owner	Cost	Acceptance
A1	Design the kitchen	Architect	USD 6,000.00	Drawings signed
A2	Apply for the permit	Project manager	USD 2,000.00	Permit issued
A3	Fit out the kitchen	Builder	USD 30,000.00	Handover signed
A4	Install equipment	Supplier	USD 10,000.00	Equipment commissioned

The schedule carries 4 activities.

ID	Activity	Duration	ES	EF	LS	LF	Float	Critical
A1	Design	10.0	0	10.0	0.0	10.0	0.0	yes
A2	Permit	15.0	10.0	25.0	10.0	25.0	0.0	yes
A3	Fit out	20.0	25.0	45.0	25.0	45.0	0.0	yes
A4	Install	5.0	45.0	50.0	45.0	50.0	0.0	yes

The WBS rolls 4 nodes up to a total of USD 48,000.00.

ID	Item	Cost
A1	Design the kitchen	USD 6,000.00
A2	Apply for the permit	USD 2,000.00
A3	Fit out the kitchen	USD 30,000.00
A4	Install equipment	USD 10,000.00
	Total	USD 48,000.00

The matrix names, for every activity, the roles the record declares as responsible and accountable, and the consulted or informed roles it states.

Activity	Name	Design	Management	Build	Equipment
A1	Design	R	A		
A2	Permit		A		
A3	Fit out		A	R	
A4	Install		A		R

The register carries 1 risk.

ID	Risk	Likelihood	Impact	Response	Owner
R1	Permit delay	Medium	High	Apply early	Project manager
